

**APPLICATION AND CERTIFICATION FOR PAYMENT**

*AIA DOCUMENT G702*

**BILL TO:** Town of New Paltz  
52 Clearwater Road  
New Paltz, NY 12561

**PROJECT:** Phase III Backup Water Supply  
Plains Road Well House

**APPLICATION NO:** 5

**Distribution to:**

OWNER

ARCHITECT

CONTRACTOR

**PERIOD TO:** 05/15/23

**FROM CONTRACTOR:** CDE Electric Co., Inc.  
PO Box 204  
685 Vernal Butler Rd.  
Cairo, NY 12413

**ARCHITECT:**

**PROJECT NOS:** B&L1881.001.002

**CONTRACT DATE:** 11/15/2021

**CONTRACT FOR:** No.2C - Electrical Construction

**CONTRACTOR'S APPLICATION FOR PAYMENT**

Application is made for payment, as shown below, in connection with the Contract. Continuation Sheet, AIA Document G703, is attached.

SEE ATTACHED SWORN STATEMENT FROM CONTRACTOR TO OWNER

- 1. ORIGINAL CONTRACT SUM \$ 591,000.00
- 2. Net change by Change Orders \$ 0.00
- 3. CONTRACT SUM TO DATE (Line 1 ± 2) \$ 591,000.00
- 4. TOTAL COMPLETED & STORED TO DATE (Column G on G703) \$ 449,279.20

- 5. RETAINAGE:**
- a. 0.05 % of Completed Work \$ 22,463.96  
(Column D + E on G703)
  - b. 0.05 % of Stored Material \$ 0.00  
(Column F on G703)

Total Retainage (Lines 5a + 5b or Total in Column I of G703) \$ 22,463.96

**6. TOTAL EARNED LESS RETAINAGE** (Line 4 Less Line 5 Total) \$ 426,815.24

**7. LESS PREVIOUS CERTIFICATES FOR PAYMENT** (Line 6 from prior Certificate) \$ 342,028.69

**8. CURRENT PAYMENT DUE** (Line 6 less Line 7) \$ 84,786.55

**9. BALANCE TO FINISH, INCLUDING RETAINAGE** (Line 3 less Line 6) \$ 164,184.76

CHANGE ORDER SUMMARY	ADDITIONS	DEDUCTIONS
Total changes approved in previous months by Owner		
Total approved this Month		
<b>TOTALS</b>	0.00	0.00
<b>NET CHANGES by Change Order</b>	0.00	

The undersigned Contractor certifies that to the best of the Contractor's knowledge, information and belief the Work covered by this Application for Payment has been completed in accordance with the Contract Documents, that all amounts have been paid by the Contractor for Work for which previous Certificates for Payment were issued and payments received from the Owner, and that current payment shown herein is now due.

**CONTRACTOR:**

*[Signature]*

**By:** \_\_\_\_\_ **Date:** 5/22/23

State of New York County of Greene  
Subscribed and sworn to before me this 22<sup>nd</sup> day of May 2023  
Notary Public: *[Signature]*  
My Commission expires: SANDRA M. SMITH  
Notary Public, State of New York

**ARCHITECT'S CERTIFICATE FOR PAYMENT**

In accordance with the Contract Documents, based on on-site observations and the Notary's Commission Expires 08-29-20 23 comprising the application, the Architect certifies to the Owner that to the best of the Architect's knowledge, information and belief the Work has progressed as indicated, the quality of the Work is in accordance with the Contract Documents, and the Contractor is entitled to payment of the AMOUNT CERTIFIED.

AMOUNT CERTIFIED ..... \$ 84,786.55

*(Attach explanation if amount certified differs from the amount applied. Initial all figures on this Application and on the Continuation Sheet that are changed to conform with the amount certified.)*

**ARCHITECT:**

*[Signature]* AS AN AGENT FOR  
LABELLA ASSOCIATES

**Date:** 5/26/23

This Certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the Contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or Contractor under this Contract.

# CONTINUATION SHEET

AIA DOCUMENT G703

Page of Pages

AIA Document G702, APPLICATION AND CERTIFICATION FOR PAYMENT, containing

APPLICATION NO.

5

Contractor's signed certification is attached.

APPLICATION DATE:

05/22/23

In tabulations below, amounts are stated to the nearest dollar.

PERIOD TO:

05/15/23

Use Column I on Contracts where variable retainage for line items may apply.

ARCHITECT'S PROJECT NO.

B&L1881.001.002

A ITEM NO.	B DESCRIPTION OF WORK	C CONTRACT VALUE	D WORK COMPLETED		E THIS PERIOD	F MATERIALS PRESENTLY STORED (NOT IN D OR E)	G		H BALANCE TO FINISH (C - G)	I RETAINAGE
			FROM PREVIOUS APPLICATION (D + E)	TOTAL COMPLETED AND STORED TO DATE (D+E+F)			% (G ÷ C)			
<b>Town of New Paltz Plains Road Well House</b>										
1	General Conditions	23,640.00	11,820.00				11,820.00	50%	11,820.00	591.00
2	Allowance	15,000.00					0.00	0%	15,000.00	0.00
3	Utility Upgrade	300,000.00	253,447.20				253,447.20	84%	46,552.80	12,672.36
4	General Wiring Material	11,390.00		2,848.00			2,848.00	25%	8,542.00	142.40
5	General Wiring Labor	26,285.00		7,886.00			7,886.00	30%	18,399.00	394.30
6	Light Fixture Material	9,400.00	5,500.00	564.00			6,064.00	65%	3,336.00	303.20
7	Light Fixture Labor	10,700.00		5,350.00			5,350.00	50%	5,350.00	267.50
8	Electrical Service Material	39,000.00	29,214.00	9,786.00			39,000.00	100%	0.00	1,950.00
9	Electrical Service Labor	20,900.00	13,585.00	7,315.00			20,900.00	100%	0.00	1,045.00
10	Underground Primary Material	12,200.00	12,200.00				12,200.00	100%	0.00	610.00
11	Underground Primary Labor	10,000.00	10,000.00				10,000.00	100%	0.00	500.00
12	Site Excavation	19,750.00	11,850.00				11,850.00	60%	7,900.00	592.50
13	Generator & ATS Material	74,000.00	11,390.00		55,500.00		66,890.00	90%	7,110.00	3,344.50
14	Generator & ATS Labor	10,235.00	1,024.00				1,024.00	10%	9,211.00	51.20
15	Lighting Protection Installation	8,500.00					0.00	0%	8,500.00	0.00
<b>GRAND TOTALS</b>		591,000.00	360,030.20	89,249.00		0.00	449,279.20	76%	141,720.80	22,463.96

# /OICE - Sales



**Please Remit To:**  
 KINSLEY GROUP, INC.  
 DEPARTMENT 2150  
 PO BOX 986500  
 BOSTON, MA 02298-6500

**Invoice Number:** IC36625  
**Invoice Date:** 4/10/2023  
**PO Number:** PRWH-KIN01  
**Total Due:** \$55,110.00

**Bill To:**  
 CDE ELECTRIC INC  
 P O BOX 204  
 CAIRO, NY 12413

**Job Address:**  
 CDE ELECTRIC INC  
 685 VERNAL BUTLER ROAD  
 CAIRO, NY 12413

**Description:** 180REOZJG Kohler 180kw generator 337RGMLF0003

THANK YOU FOR CHOOSING KINSLEY POWER!

**Job:** J-21-1428 - PLAINS RD WELL HOUSE CONSTRUCT

*New Part*

Salesperson	Customer Number	Contract Number	Payment Terms	Due Date	Shipping Method
	018945		NET 30 PRIOR TO S/U	5/10/2023	BWY

Bill Code Number	Description	S/N	Current Bill
2-200	180REOZJG		\$55,110.00

Billing Amount: \$55,110.00  
 Retention Withheld: \$0.00  
 Retention Due: \$0.00  
 Subtotal: \$55,110.00  
 Miscellaneous: \$0.00  
 Total Tax: \$0.00  
**Total: \$55,110.00**

**Ilker, Kurt**

---

**From:** Gregory Guerin - CDE Electric <gguerin@cdeelectric.net>  
**Sent:** Monday, May 22, 2023 7:18 AM  
**To:** Ilker, Kurt  
**Cc:** Aber, Gary  
**Subject:** [Ext] FW: Generator  
**Attachments:** image000001(1).jpg; image000000(1).jpg; image000001.jpg; image000000.jpg

Kirk

Here are some pictures of the Generator

Greg

**From:** Gregory Guerin - CDE Electric <gguerin@cdeelectric.net>  
**Sent:** Monday, May 22, 2023 7:16 AM  
**To:** Gregory Guerin - CDE Electric <gguerin@cdeelectric.net>  
**Subject:**

Sent via the Samsung Galaxy S10, an AT&T 5G Evolution capable smartphone

**CAUTION:** This email originated from outside the LaBella organization. Do not click links or open attachments unless you recognize the sender and know the content is safe.

**SYSTEM  
CAN CAUSE  
ELECTROCUTION OR  
PROPERTY DAMAGE.**

**FOR STANDBY POWER,  
USE OF AUTOMATIC TRANSFER  
SWITCH IS RECOMMENDED  
TO PREVENT INADVERTENT  
INTERCONNECTION  
OF STANDBY AND NORMAL  
SOURCES OF SUPPLY.**

04107342

# KOHLER

Genset Model	180REOZJG				
Spec Number	GM84750 - GA1				
Serial Number	337RGMLF0003				
Material	180REOZJG - CP1				
Service Duty	STANDBY	Amps	271	kW	180
	180	Phase	3	kVA	225
		RPM	1800	PF	0.8
		Battery	24V	Hz	60
	0123	Fuel	DIESEL		


Stationary Engine Generator Assembly  
UL2200 Requirements are met at 25°C  
Ambient (Per UL Standard Test)

Max Fuel Flow: 24.00 GPH

Made in USA by Kohler Co.  
1000 Drive Kohler, WI 53044  
248-2444 KohlerPower.com




**DANGER**



**...VOLTAGE AND ROTATING PARTS  
...WARNING**


**UNBALANCED WEIGHT.  
IMPROPER LIFT CAN CAUSE PERSONAL  
AND EQUIPMENT DAMAGE.  
USE BOTH LIFTING EYES WHEN P  
DO NOT APPLY FORCE TO FAN OR  
WHEN LIFTING.  
FOR GENERATORS WITHOUT LIFT  
SECURE CHAIN TIGHTLY AROUND  
END BRACKET LIFTING RIB.**


**LIFTING METHOD**

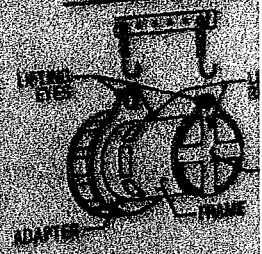

**DO NOT LIFT COMPLETE GENERATOR  
LIFTING EYES.  
USE LIFTING BARS THRU HOLES IN**

**SLING METHOD**



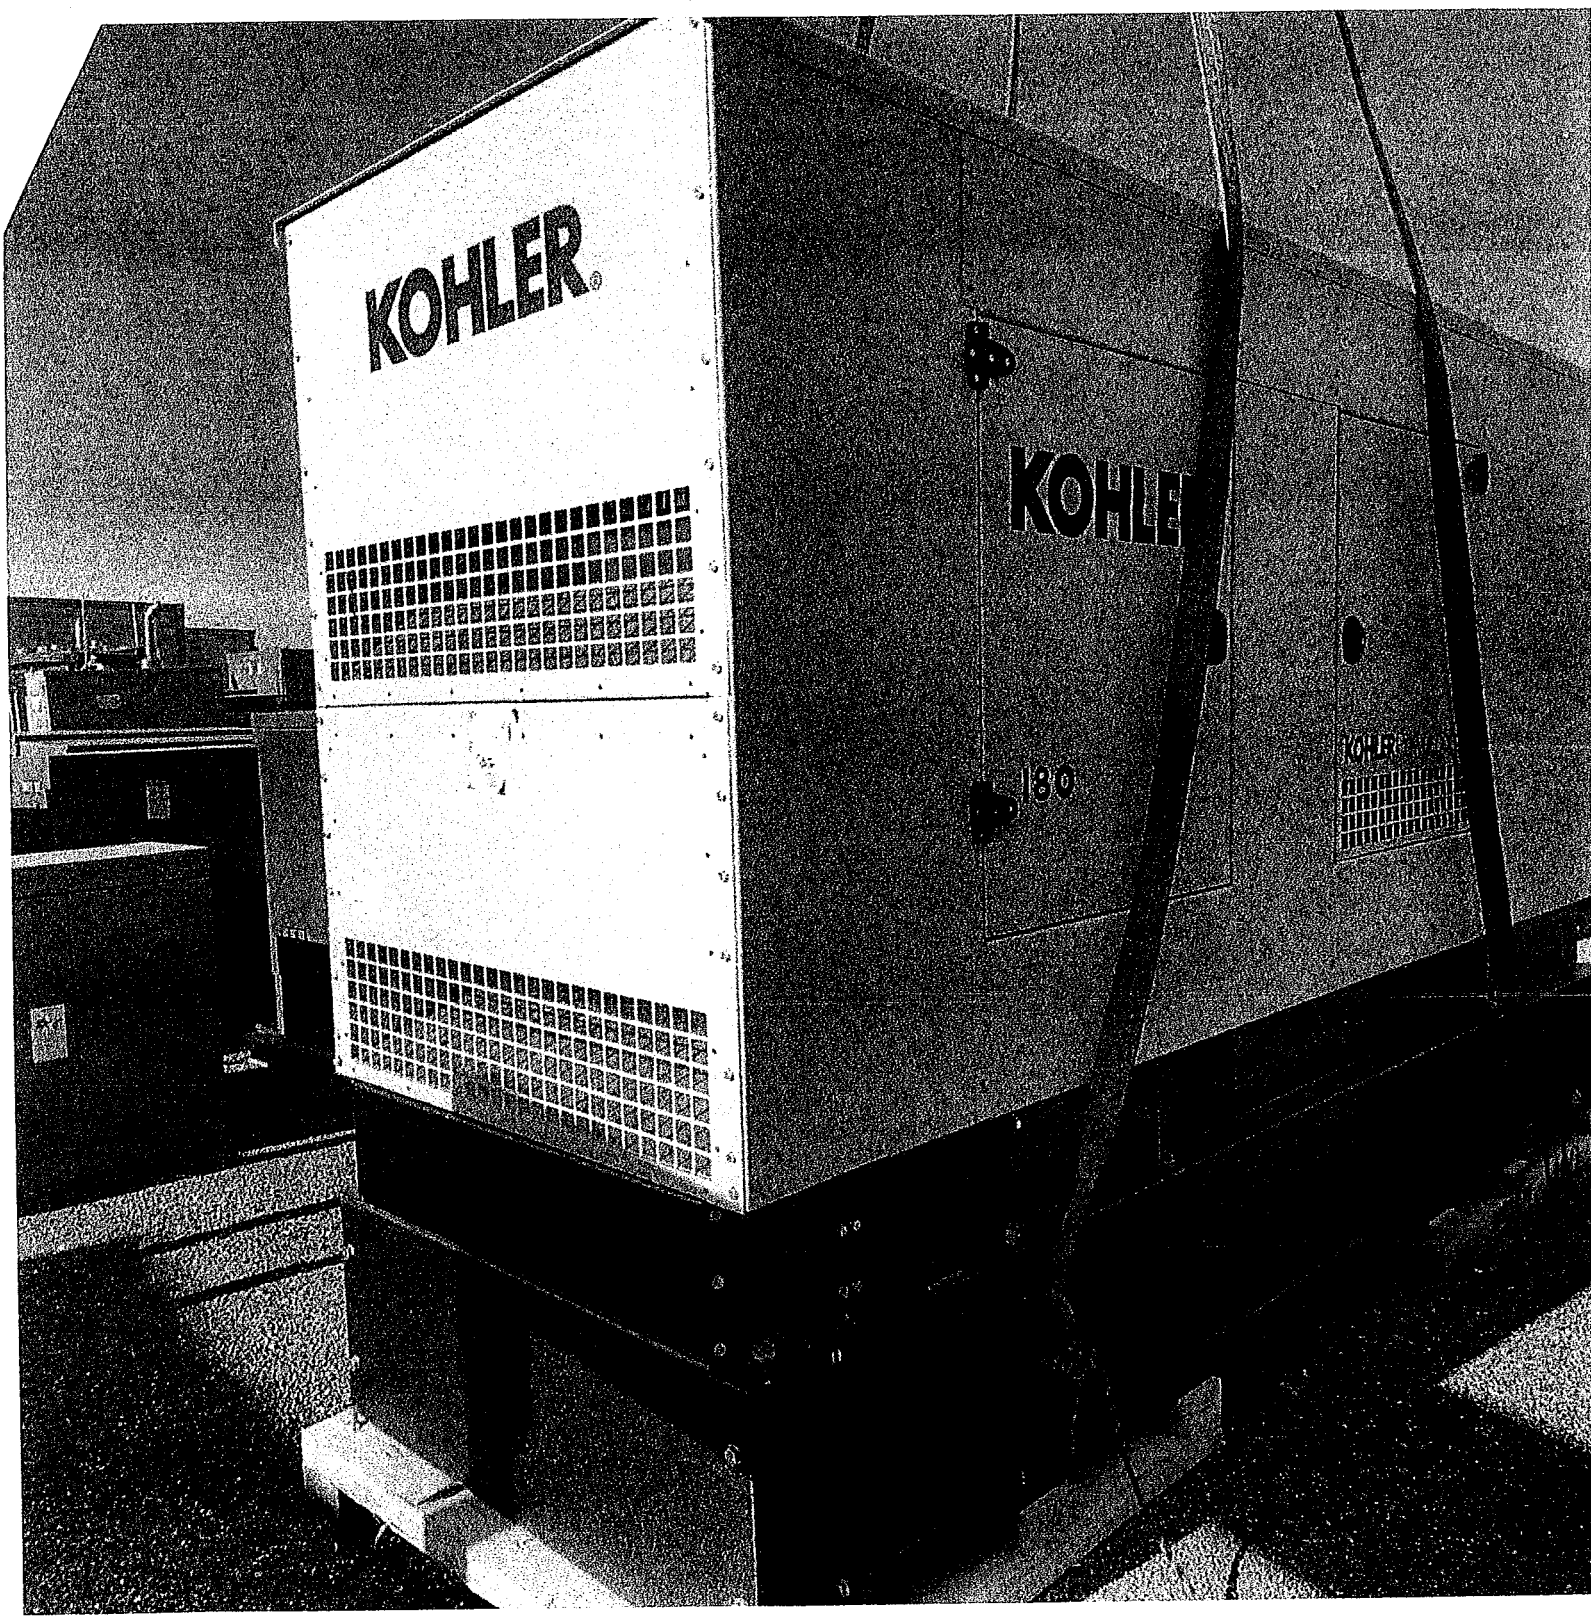

**KOHLER**

**KOHLER**

130

**KOHLER**

NAME OF CONTRACTOR <input checked="" type="checkbox"/> OR SUBCONTRACTOR		ADDRESS																	
CDE Electric, Inc.		PO Box 204, 685 Vernal Butler Rd., Cairo, NY 12414																	
FEIN		PROJECT AND LOCATION																	
27-2051468		Town of New Paltz Phase III Backup Water Supply Plains Road Well House																	
FOR WEEK ENDING		CONTRACT NO																	
4/1/23																			
Employee Name Address ID No	Work Classification	Day and Date							Total Hours	Rate of Pay	Gross Amount Earned	Deductions				Net Wages Paid for Week			
		S	M	T	W	T	F	S				FICA	Fed	State	DBL/PFL		Other		
		26	27	28	29	30	31	1											
Gregory E. Guerin ...3110 87 Manorwoods Round Top, NY 12473	Corporate Officer Electrician								0.00	86.12	0.00								
Timothy A. Jones ...6739 856 Route 23A Catskill, NY 12414	Corporate Officer Electrician								0.00	86.12	0.00								
Douglas R. Bruck ...5179 436 County Rt. 39 Round Top, NY 12473	Electrician								0.00	86.12	0.00								
Aaron J. Mossman ...1107 152 White Birch Rd. Hudson, NY 12534	Electrician								0.00	86.12	0.00								
Mark A. Jones ...3101 856 Route 23A Catskill, NY 12414	Electrician								0.00	86.12	0.00								
												3,276.32	248.44	344.72	164.64	15.51	371.71	2,131.30	
Timothy A. Jones ...6739 856 Route 23A Catskill, NY 12414	Corporate Officer Excavator Operator								0.00	93.72	0.00								
Douglas R. Bruck ...5179 436 County Rt. 39 Round Top, NY 12473	Skid Steer Operator								0.00	90.22	0.00								
												3,276.32	235.57	540.34	179.38	15.51	721.17	1,584.35	



















